Federal Way Link Extension

Project Update & Motion No. M2025-10

System Expansion Committee 2/13/2025



Why are we here

- Federal Way Link Extension Project Status Update
- Motion No. M2025-10: Authorizing additional contingencies within the baseline budget





Federal Way Link Extension







Federal Way Link Extension









Financial Snapshot

Project Budget	\$2.451 B
Committed	\$2.121 B
Incurred	\$2.008 B

Year of Expenditure \$


- Project is 94% complete
- FWLE progress schedule forecast opening Q1 2026



[•] Financials and progress as of December 2024

Schedule to Complete

- Coordinating closely with Design-Builder to maintain testing progress
- On track for Q1 2026 Revenue Service

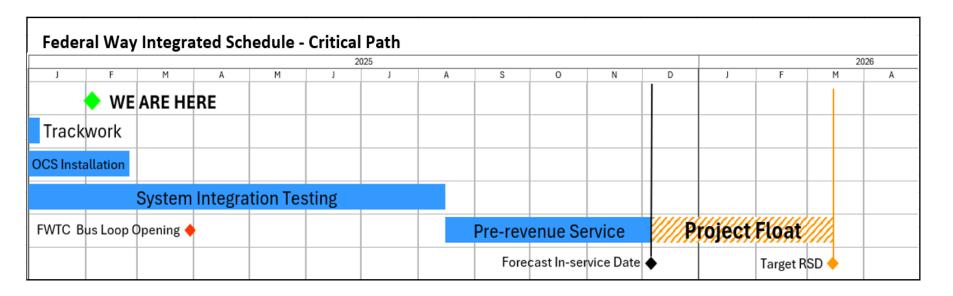

Today's action:

Motion No. M2025-10: Authorizes the chief executive officer to increase certain Federal Way Link Extension contract and/or agreement amounts as necessary, for a total authorized cumulative increase not to exceed \$60,000,000, all within the Federal Way Link Extension approved baseline budget.



Thank you.



soundtransit.org





