


# Federal Way Link Extension

Project Update March 2018






# Kent/Des Moines Station Area

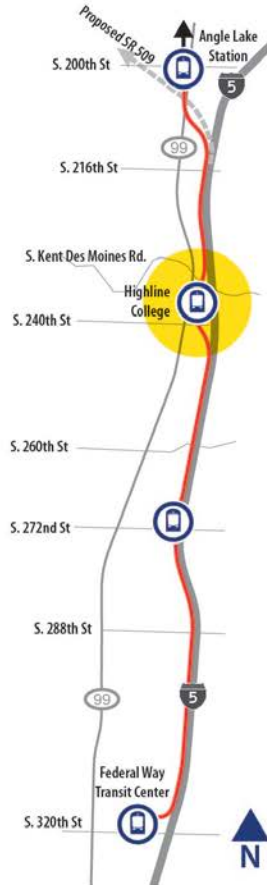

**DRAFT**  
For illustration and discussion purposes only.




# South 272nd Street Station Area

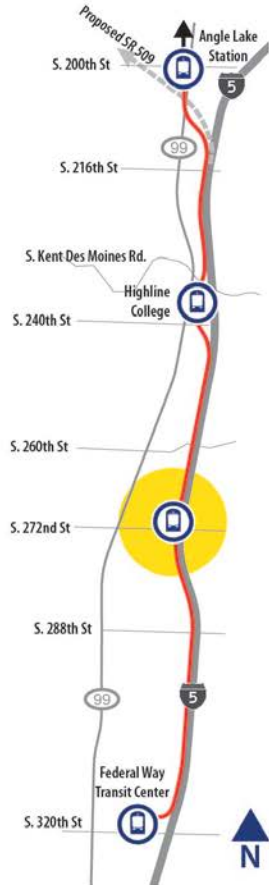

**DRAFT**  
For illustration and discussion purposes only.

# Federal Way Transit Center Station Area

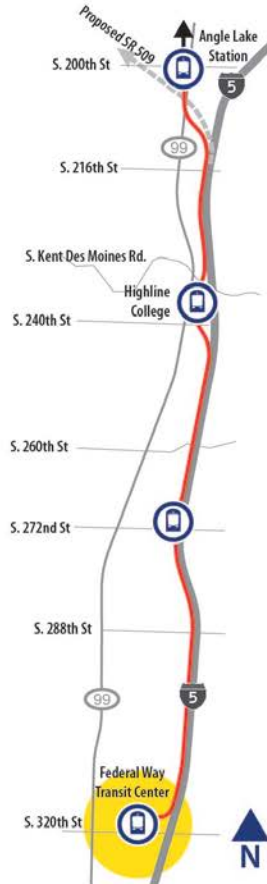

**DRAFT**  
For illustration and discussion purposes only.

# Federal Way Link Extension

## 2015 - 2025 Project Timeline




DRAFT

Project allocation to date

**\$412M**

Phase Gate 4 authorized (2017)

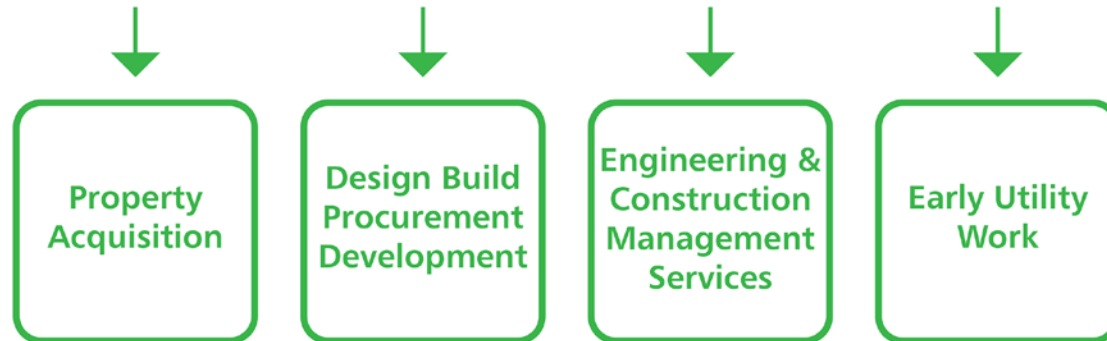

Project to be baselined in late 2018

## Public Outreach



- Relocation workshops
- Neighborhood briefings
- One on one property owner meetings



## Stakeholder Collaboration

- Code & ordinance updates
  - Bus routing & layover
  - Housing relocation coordination

12

### Cities & Agencies

City of Des Moines  
 City of Kent  
 City of Federal Way  
 WSDOT  
 King County Metro  
 Pierce Transit  
 Highline College  
 South King Council of Human Services  
 Transportation Choices Coalition  
 Federal Way Chamber of Commerce  
 Federal Way Community Connections  
 Federal Way Planning Commission



## Agreements and Permitting



## Design Build Activities

- RFQ
- RFP
- Industry outreach






- SR 509 project team coordination
  - Airspace lease
    - Temporary construction
      - SR 99 bridge discussions





## Property Acquisition

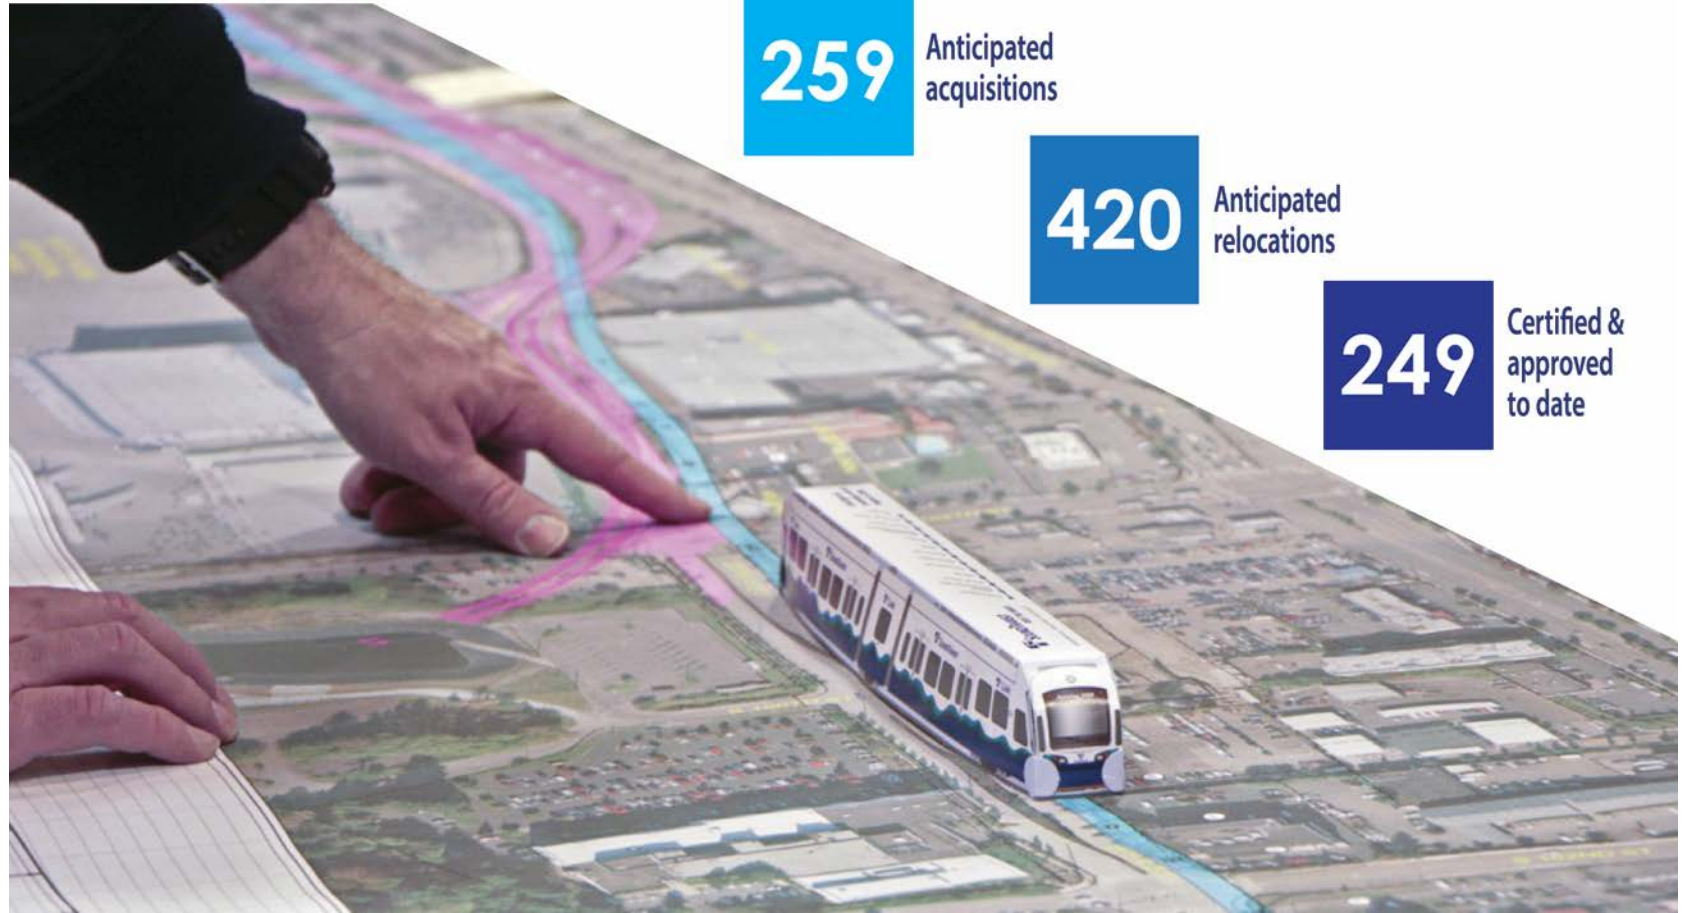

259

Anticipated  
acquisitions

420

Anticipated  
relocations

249


Certified &  
approved  
to date

## Top Risks

- FFGA uncertainty at Federal level may impact schedule
- Property acquisition and relocations completed in time for construction
- Construction market conditions - competition, price escalation, labor shortages
- Timely third party approvals - FTA, Cities, WSDOT, FHWA



## Next Steps

- 
- 2018 ● Complete ROW certification
  - 2018 ● Finalize our Transit Way and Development agreements with the Cities
  - 2018 ● Issue the Design Build Request For Proposal
  - 2018 ● Baseline the project and seek approval to enter phase gate 5
  - 2018 ● Finalize and submit FFGA application
  - 2019 ● Execute FFGA
  - 2019 ● Issue Notice to Proceed to Design Build contractor
  - 2020 ● Complete ROW acquisition
  - 2024 ● Begin Revenue Service





 **SOUNDTRANSIT**  
RIDE THE WAVE
