
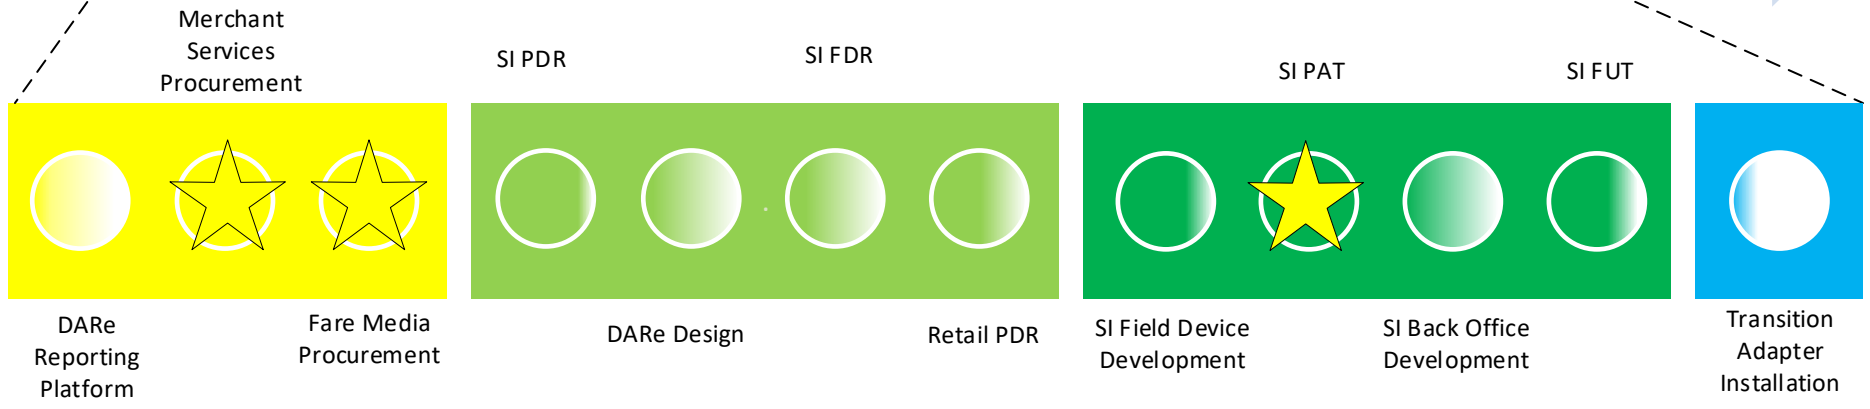


# next generation ORCA Monthly Program Dashboard

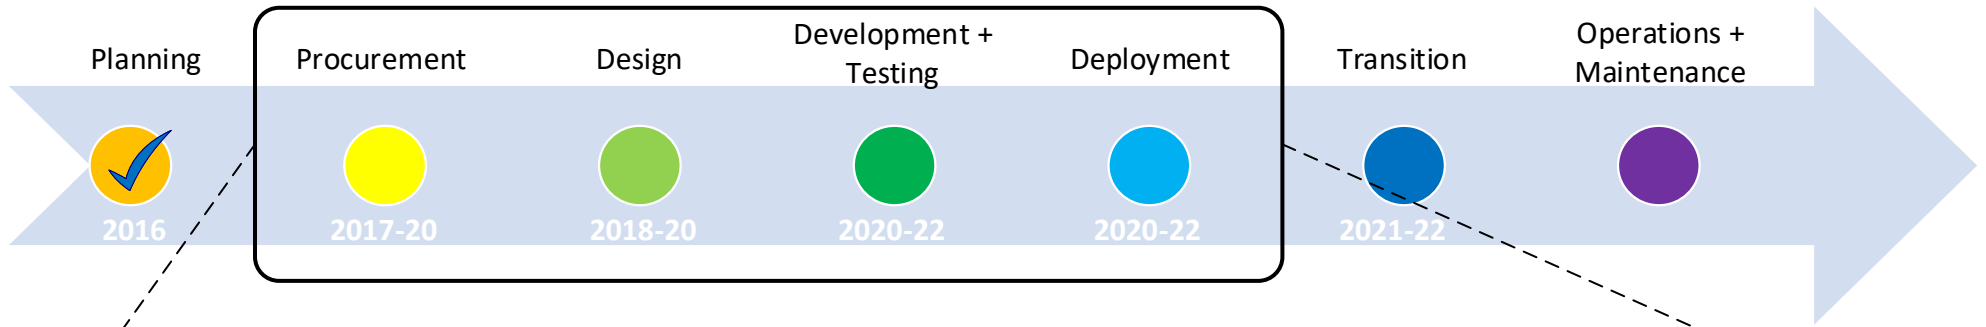

<u>Actions Complete</u> (in last ~two months)		
<input checked="" type="checkbox"/>	SI Functional Unit Test – CRM Pt. 1 Completed	9/23/20
<input checked="" type="checkbox"/>	Legacy DARE Soft Launch	10/2/20
<input checked="" type="checkbox"/>	SI Production Acceptance Test Phase Completed	10/6/20
<input checked="" type="checkbox"/>	SI Functional Unit Test – Backoffice Completed	10/23/20
<input checked="" type="checkbox"/>	SI FUT – CRM Pt. 2 and Third Parties Completed	11/13/20

<u>Upcoming Actions Anticipated</u> (in next ~two months)		
<input type="checkbox"/>	SI Functional Unit Test Phase Complete	12/31/20
<input type="checkbox"/>	Retail Network Preliminary Design Complete	12/31/20
<input type="checkbox"/>	SI Preliminary Design Complete	1/29/21
<input type="checkbox"/>	SI Final Design Substantial Completion	2/26/21
<input type="checkbox"/>	SI System Integration Test Begins	3/1/21

Program Status	
	Schedule (crit. path on track)
	Budget (within target)
	Risk (balanced, 20% high)

Legend	
Symbol	Description
<input type="checkbox"/>	To do
<input checked="" type="checkbox"/>	Done
	Complete
	In progress
	Just completed
